ID	Task Name
1	**Development of implementation planning and communication documents**
2	Kick-off meeting
3	Prepare and finalize detailed workplan
4	*Detailed workplan*
5	Develop a monitoring and evaluation plan and impact statement form
6	*M&E Plan and Impact Statement Form*
7	**Structured stakeholder engagement**
8	Identification and outreach to key stakeholders for engagement
9	Development of agenda and material for the stakeholder engagement workshop
10	*Agenda and presentation material for the stakeholder engagement workshop*
11	Facilitation of 0.5-day stakeholder engagement meeting
12	*Stakeholder workshop and inception report*
13	**Framework and methodology for vulnerability assessments**
14	Flight mission for testing of identified parameters
15	Development of technical specifications
16	*Technical report on UAV and Remote Sensing Specifications*
17	Development of a framework for UAV and remote sensing technologies in agriculture
18	*Framework for UAV and Remote Sensing for agricultural applications*
19	**Collection of pilot baseline data and development of case study**
20	Piloting of technologies for collection of a baseline dataset
21	Development of case study
22	*Pilot case study report*
23	**Training on UAV and remote sensing technologies**
24	Identification of training participants and development of training materials
25	*Agenda and course material for UAV and Remote Sensing applications*
26	Facilitation of a 5 day training on UAV and remote sensing technologies
27	*Training feedback form*
28	Write training report
29	*Training report*

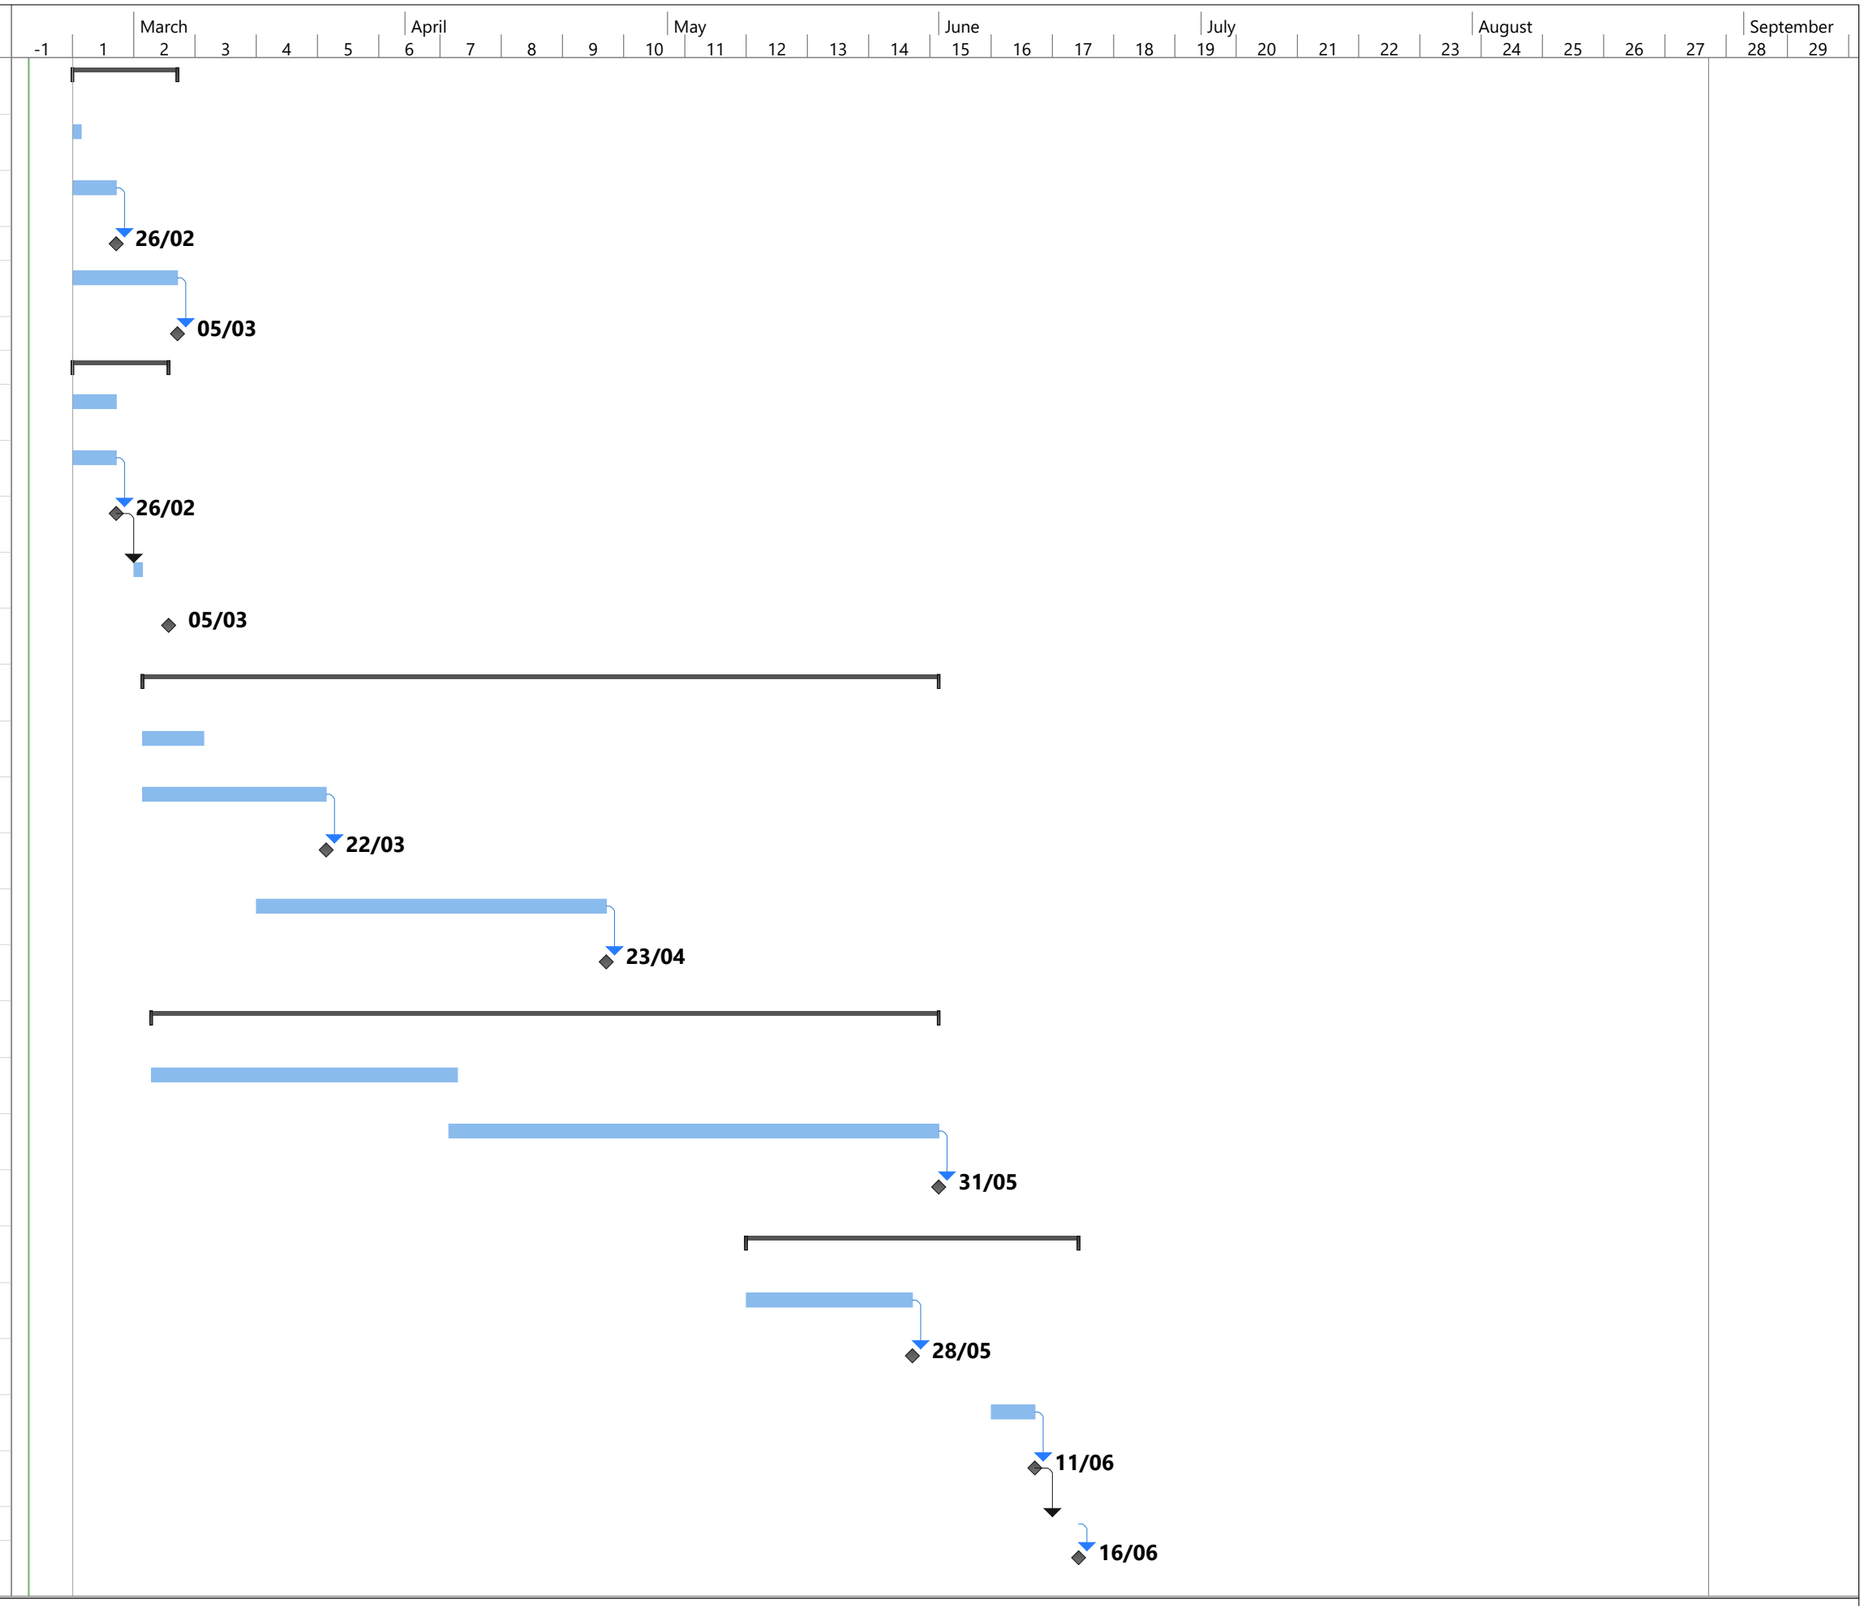

Project: Eswatine Drones for DR
Date: Wed 17/02/21

Task | Split | Milestone | Summary | Project Summary | Progress

ID	Task Name
30	**Support for identifying financing opportunities to create enabling environment to upscale deployment and use of UAV and remote sensing technologies**
31	Development of a GCF Readiness proposal
32	*GCF Readiness Proposal*
33	**Technical Assistance Close out**
34	Development of final technical assistance report
35	*Final report/End of Technical assistance report*

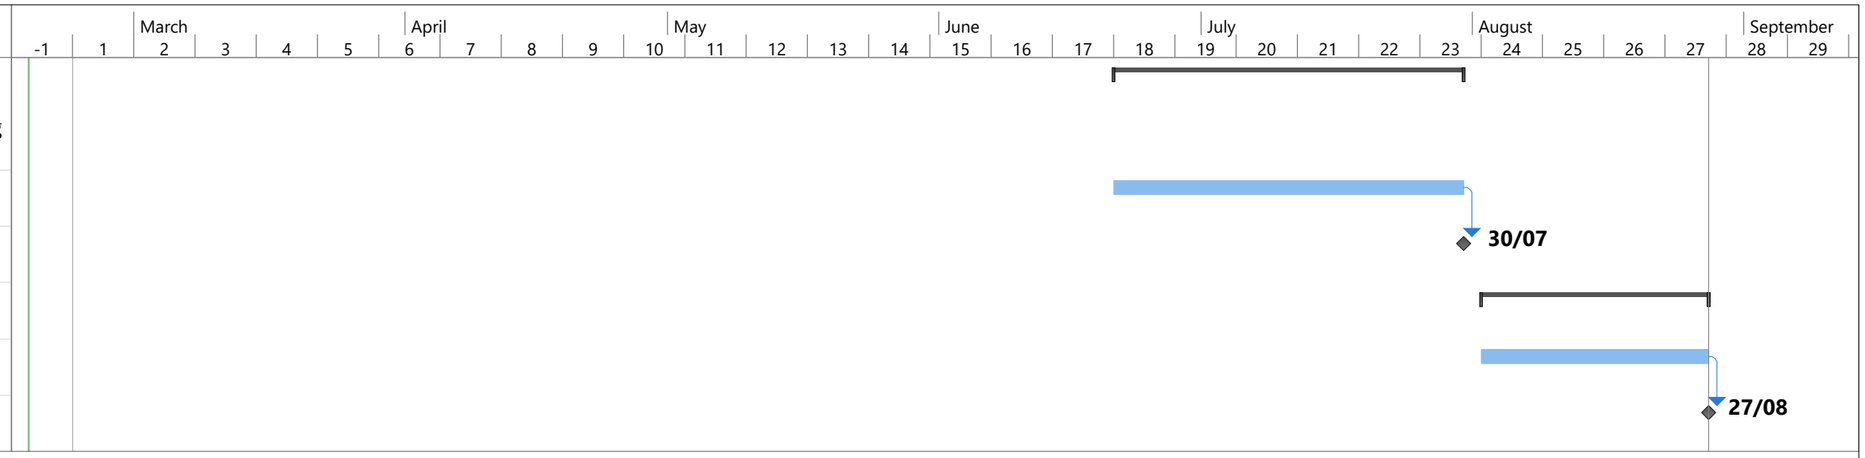

Project: Eswatine Drones for DR
Date: Wed 17/02/21

Task | Split | Milestone | Summary | Project Summary | Progress
